


1. Using a simple table.

Task (Activity)	Duration (days)	Start/End Date	Predecessor
A (Requirements Analysis)	4	28 Apr - 01 May	-
B (Database Schema Design)	3	02 May - 04 May	A
C (Backend Development)	7	05 May - 11 May	B
D (Frontend Development (UI))	5	05 May - 09 May	B
E (Hardware Integration)	6	12 May - 17 May	C
G (User Documentation)	3	10 May - 12 May	D
F (System Testing)	4	18 May - 21 May	D, E
H (Deployment)	2	22 May - 23 May	F, G

2. Using a bar chart (Gantt chart)

D a y s	28	29	30	01	02	03	04	05	06	07	08	09	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27
A																														
B																														
C																														
D																														
E																														
G																														
F																														
H																														

3. Using a graph (PERT diagram)

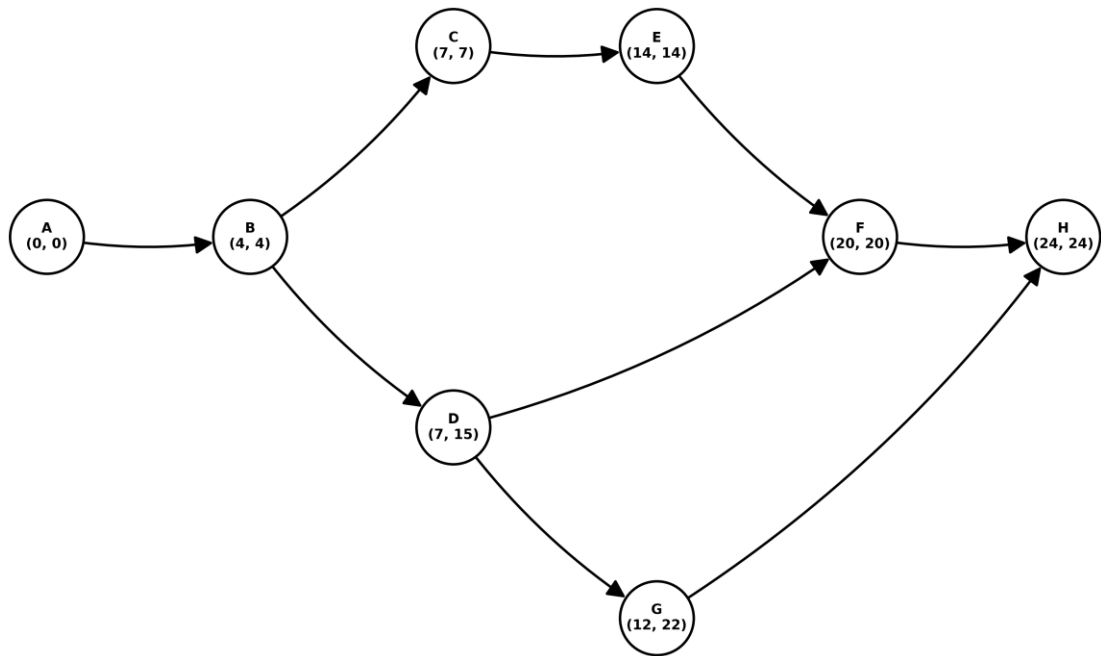

4. Critical Path Analysis

The Critical Path is A -> B -> C -> E -> F -> H.
